


Activity ID	Responsible Party	Activity Name	Duration	Start	Finish	Predecessors	Successors	2016				2017				2018				2019				2020				2021				2022				2023			
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
<b>Project Management</b>																																							
<b>Stages and Approval Gates</b>																																							
<b>General (MPO Execution Staff)</b>																																							
5500	MPO Execution PM	Gate 5 - Prepare Initial PLSC & TSPOC Presentations & Send to Team	7	07-Aug-19	15-Aug-19	5420, 6800, 7020, 7020	5505, 5510																																
5505	MPO Execution PM	Gate 5 - Review & Approval by Department M3's	8	16-Aug-19	27-Aug-19	5500	5515																																
5510	MPO Execution PM	Gate 5 - Review & Approval by Business Unit Directors	8	16-Aug-19	27-Aug-19	5500	5515																																
5515	MPO Execution PM	Gate 5 - Final Approval - TBDU SVP Sign-Off	7	28-Aug-19	06-Sep-19	5510, 5505	5520																																
5520	MPO Execution PM	Gate 5 - Finalize PLSC & TSPOC Presentations	2	09-Sep-19	10-Sep-19	5515	5525																																
5525	MPO Execution PM	Gate 5 - PLSC Committee Presentation & Approval	0		18-Sep-19	5520	5530																																
5530	MPO Execution PM	Gate 5 - TSPOC Committee Presentation & Approval	0		25-Sep-19	5525	5535																																
5535	MPO Execution PM	Gate 5 - Complete	0		25-Sep-19	5530	5850																																
5590		Pre-Construction Planning - Stage 5 - Finish	0		23-Jun-20	5950, 6610, 7020, 7020																																	
5600	MPO Execution PM	Prepare & Issue ATP for Final Engineering & Real Properties	10	08-Jun-18	21-Jun-18	5200	7000, 6255, 5650, 5650																																
5650	MPO Execution PM	Prepare & Issue ATP for Procurement & Permitting	10	02-Aug-18	15-Aug-18	5240, 5600	7520, 5950, 6610, 6610																																
5800	CEHS	CEHS - Conduct Environmental Surveys & Prepare Mitigation Plans	126	07-Jun-19	06-Dec-19	7500, 6200, 6800, 6800	5810, 5590																																
5810	RP&A	RP&A - Prepare & Submit NTP	63	22-Nov-19	26-Feb-20	5800, 6204	5820																																
5820	CPUC	CPUC Reviews & Issues NTP	63	28-Jan-20	24-Apr-20	5810	5850																																
5850	MPO Execution PM	Prepare & Issue ATP's for Construction	10	27-Apr-20	08-May-20	5535, 5820	5900																																
5900		Construction - Stage 6 - Start	0		11-May-20	5850	6440, 7050, 6650, 6650																																
5950	CEHS	Additional Licenses & Permits	251	25-Jan-19	24-Jan-20	6200, 5650	5590, 6250, 6652, 6652																																
9100	MPO Execution PM	FORECASTED In-Service Date	0		18-Apr-23	7060, 7590	9200																																
9110	MPO Execution PM	APPROVED In-Service Date	0		02-Jan-20*																																		
9200		Construction - Stage 6 - Finish	0		19-Apr-23	9100	9500																																
9500	MPO Execution PM	Project Close-Out	126	19-Apr-23	16-Oct-23	9200																																	
<b>Licensing</b>																																							
<b>Licensing Project Management, Administration and Initiation</b>																																							
4000	SCE	Application Production - Stage 4 - Start	0	02-Jan-15 A			4820																																
4700	MPO Developmen	PEA Complete - N/A - SCE will utilize the City of Riverside's Certified EIR (Assumes the CPUC will not be "Lead Agency")	0		02-Jan-15 A																																		
4800	P&PR	Class III Estimate - Request Department Estimates	0		14-Jan-15 A		4802																																
4802	Functional Depts.	Class III Estimate - Functional Departments Start Preparation of Department Estimates	0	15-Jan-15 A	11-Feb-15 A	4800	4806																																
4806	P&PR	Class III Estimate - Verification & Aggregation of Department Estimates	0	12-Feb-15 A	19-Feb-15 A	4802	4808																																
4808	MPO Developmen	Class III Estimate - Final Review & Approval by Project Team & MPO M3	0	20-Feb-15 A	26-Feb-15 A	4806	4810																																
4810	Treasurer	Class III Estimate - CRT Package to Treasurer, for Review & Approval	0	27-Feb-15 A	04-Mar-15 A	4808	4812																																
4812	P&PR	Class III Estimate - Management Review - with Maria Charca & Kevin Cini	0	05-Mar-15 A	13-Mar-15 A	4810	4814																																
4814	P&PR	Class III Estimate - Management Review - with Pete Deitrich	0	16-Mar-15 A	26-Mar-15 A	4812	4844																																
4820	Law	CPCN Application - Prepare CPCN Application	0	02-Jan-15 A	10-Feb-15 A	4000	4850, 4822																																
4822	Project Team	CPCN Application - Final Review & Approval by Project Licensing Team	0	11-Feb-15 A	18-Feb-15 A	4820	4830																																
4830	MPO Developmen	Gate 4 - Prepare PLSC & TSPOC Presentations & Send to Team	0	19-Feb-15 A	23-Feb-15 A	4822	4832																																
4832	MPO Developmen	Gate 4 - Review & Approval by Department M3's	0	24-Feb-15 A	27-Feb-15 A	4830	4838																																
4838	MPO Developmen	Gate 4 - Finalize PLSC & TSPOC Presentations	0	02-Mar-15 A	02-Mar-15 A	4832	4840																																
4840	MPO Developmen	Gate 4 - Presentation to PLSC Committee	0		03-Mar-15 A	4838	4842																																
4842	MPO Developmen	Gate 4 - Presentation to TSPOC Committee	0		10-Mar-15 A	4840	4844																																
4844	MPO Developmen	Gate 4 - Presentation to CRT Committee	0		31-Mar-15 A	4814, 4842	4846																																
4846	MPO Developmen	Gate 4 - Complete	0		10-Apr-15 A	4844	4850																																
4850	Case Admin. / MPO	CPCN Application & City of Riverside's Certified EIR - Printing & Proof Reading	0	13-Apr-15 A	14-Apr-15 A	4820, 4846	4880																																
4880	Law	CPCN Application - Original Filing with CPUC & Other Agencies	0		15-Apr-15 A	4850	4924, 4934, 4920, 4920																																
4882	Law	CPCN Application - Amended Filing with CPUC & Other Agencies	0		30-Apr-15 A	4880	4900, 4930, 4890, 4890																																
4890	Subtransmission	CPCN Application - Post "Notice of Filing"	0		01-May-15 A	4882	4940																																
4900	Law	CPCN Application - File Declaration (by Statute, 5 calendar days after Filing)	0		05-May-15 A	4882	4940																																
4910	Case Administration	CPCN Application - Send Mailings (300' List, etc.)	0		01-May-15 A	4882	4940																																
4920	LPA	CPCN Application - Original Application - Run First Advertisement in Press Enterprise (Main Publication)	0	15-Apr-15 A	15-Apr-15 A	4880	4922																																
4922	LPA	CPCN Application - Original Application - Run Second Advertisement in Press Enterprise	0	22-Apr-15 A	22-Apr-15 A	4920	4940																																
4924	LPA	CPCN Application - Original Application - Run First Advertisement in Riverside Record (Secondary Publication)	0	15-Apr-15 A	15-Apr-15 A	4880	4926																																
4926	LPA	CPCN Application - Original Application - Run Second Advertisement in Riverside Record	0	22-Apr-15 A	22-Apr-15 A	4924	4940																																
4930	LPA	CPCN Application - Amended Application - Run First Advertisement in Press Enterprise (Main Publication)	0	30-Apr-15 A	30-Apr-15 A	4882	4932																																
4932	LPA	CPCN Application - Amended Application - Run Second Advertisement in Press Enterprise	0	07-May-15 A	07-May-15 A	4930	4940																																
4934	LPA	CPCN Application - Amended Application - Run First Advertisement in Riverside Record (Secondary Publication)	0	14-May-15 A	14-May-15 A	4880	4936																																
4936	LPA	CPCN Application - Amended Application - Run Second Advertisement in Riverside Record	0	21-May-15 A	21-May-15 A	4934	4940																																
4940	Third Party Interve	CPCN Application - Public Protests Due Date (by Statute, 30 calendar days after "Notice of Filing")	0		01-Jun-15 A	4900, 4936, 4932, 4932	4950																																
4950	Law	CPCN Application - Due Date for SCE Reply to Protests (by Statute, 10 calendar days after Third-Party Protests Due Date)	0		11-Jun-15 A	4940	4990																																
4990		Application Production - Stage 4 - Finish	0		11-Jun-15 A	4950	5030																																
5000		Pre-Construction Planning - Stage 5 - Start	0	16-Apr-15 A		4880	5002																																
5002	CPUC	CPUC First Completeness Review	0	16-Apr-15 A	22-May-15 A	5000, 4882	5005																																
5005	CPUC	CPUC Issues Deficiency Report #1	0		22-May-15 A	5002	5006																																
5006	RP&A	SCE Completes All Responses to Deficiency Report #1	0		26-May-15 A	5005	5030																																
5010	CPUC	CPUC Issues Deficiency Report #2	0		08-Oct-15 A		5012																																
5012	RP&A	SCE Completes All Responses to Deficiency Report #2	0		09-Nov-15 A	5010	5030																																
5013	CPUC	CPUC Issues Deficiency Report #3	0		22-Oct-15 A		5023																																
5023	RP&A	SCE Completes All Responses to Deficiency Report #3	0		23-Dec-15 A	5013	5030																																

■ Completed Activity    ■ Outstanding Milestone  
■ Outstanding Activity    ■ Critical Path Milestone  
■ Critical Path Activity  
■ Completed Milestone

DRAFT

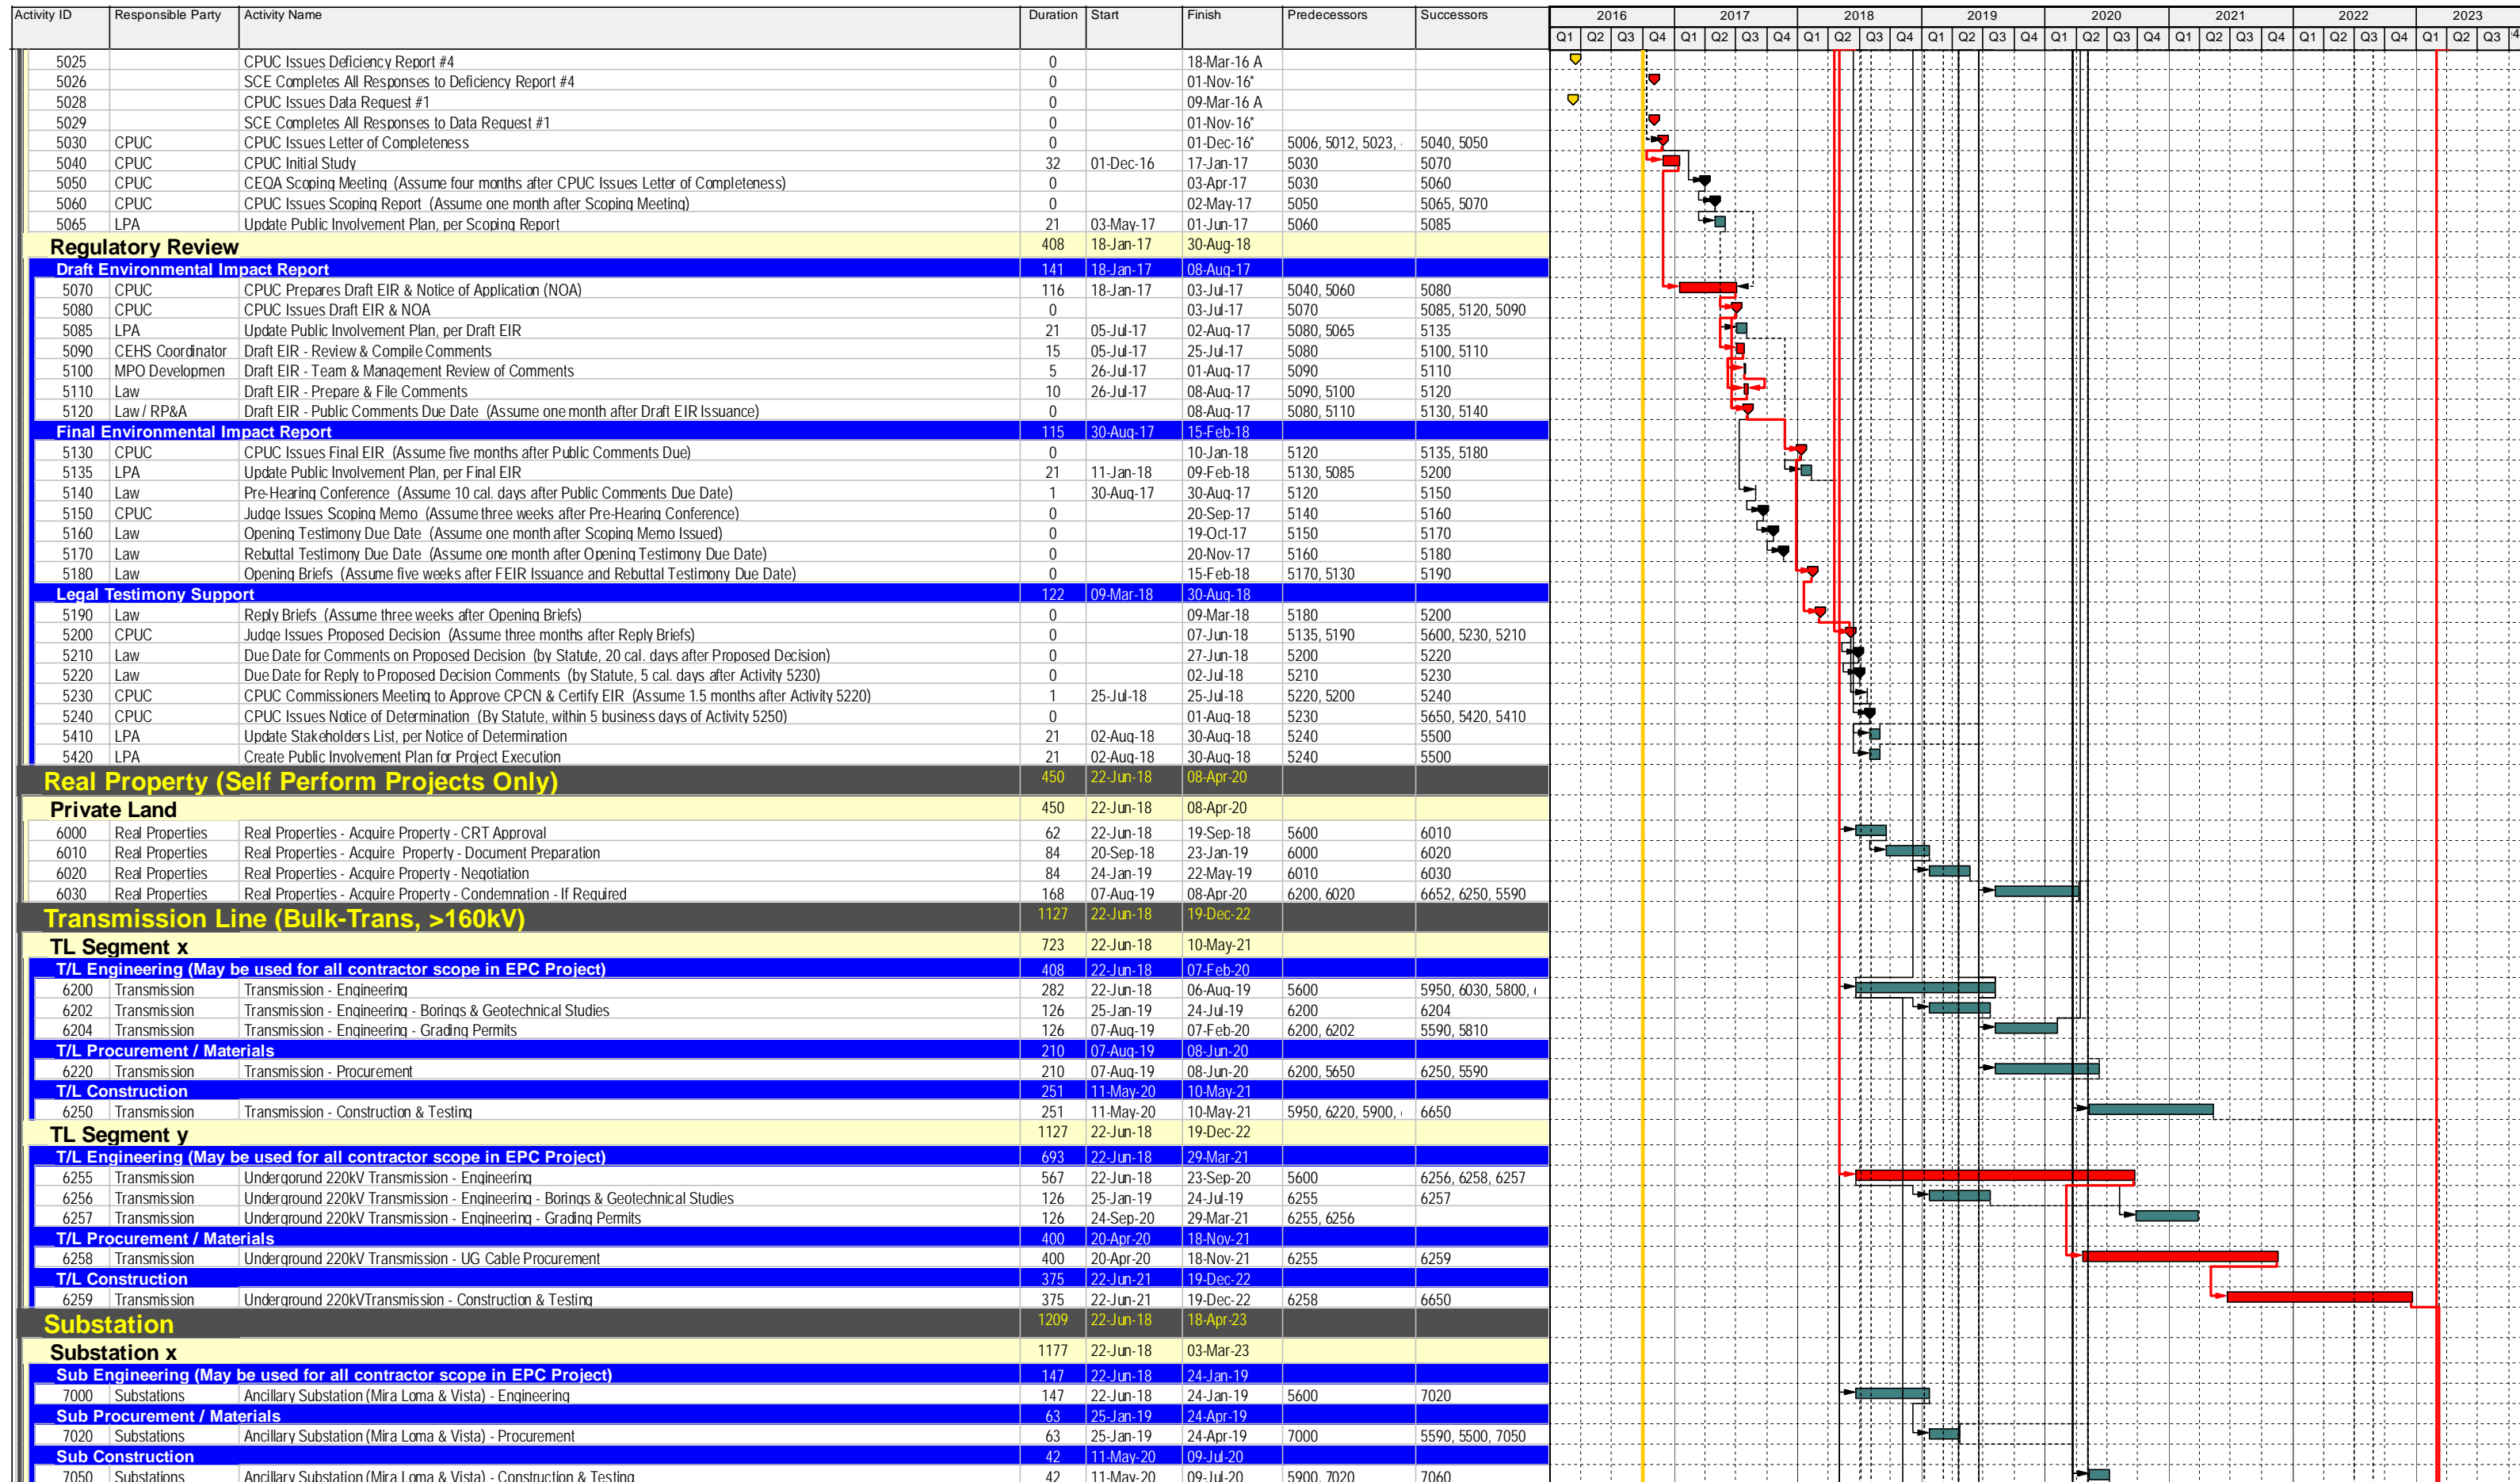

Completed Activity   
  Outstanding Activity   
  Critical Path Activity   
  Completed Milestone   
  Outstanding Milestone   
  Critical Path Milestone

**DRAFT**

Activity ID	Responsible Party	Activity Name	Duration	Start	Finish	Predecessors	Successors	2016				2017				2018				2019				2020				2021				2022				2023					
								Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4		
<b>Sub Commissioning</b>																																									
7060	Substations	Ancillary Substation (Mira Loma & Vista) - In-Service Testinq	10	17-Feb-23	03-Mar-23																																				
<b>Substation y</b>																																									
<b>Sub Engineering (May be used for all contractor scope in EPC Project)</b>																																									
7500	Substations	Wildlife Substation - Engineering	251	22-Jun-18	21-Jun-19																																				
7500	Substations	Wildlife Substation - Engineering	251	22-Jun-18	21-Jun-19	5600	7520, 7522, 5800, !																																		
<b>Sub Procurement / Materials</b>																																									
7520	Substations	Wildlife Substation - Procurement - Major Material (excl. MEER)	251	21-Sep-18	20-Sep-19	5650, 7500	7550																																		
7522	Substations	Wildlife Substation - Procurement - MEER	251	21-Jun-19	22-Jun-20	7500	7550, 5590																																		
<b>Sub Construction</b>																																									
7550	Substations	Wildlife Substation - Construction & Testinq	210	11-May-20	12-Mar-21	7520, 5900, 5950, !	7590																																		
<b>Sub Commissioning</b>																																									
7590	Substations	Wildlife Substation - Commissioning & In-Service Testinq	42	17-Feb-23	18-Apr-23	6850, 6440, 7550	9100																																		
<b>IT/Telecom</b>																																									
<b>IT/Telecom Location x</b>																																									
<b>IT/Telecom Engineering</b>																																									
6800	Telecom	Telecom - Engineering	168	22-Jun-18	25-Feb-19	5600	6810, 6600, 5500, !																																		
<b>IT/Telecom Procurement</b>																																									
6810	Telecom	Telecom - Procurement	63	26-Feb-19	23-May-19	6800, 5650	5590, 6850																																		
<b>IT/Telecom Construction</b>																																									
6850	Telecom	Telecom - Construction & Testinq	84	14-Oct-22	16-Feb-23	6650, 5900, 6810, !	7060, 7590																																		
<b>ECS</b>																																									
<b>ECS Sgement x</b>																																									
<b>ECS Engineering</b>																																									
6600	ECS	ECS - Engineering	126	22-Aug-18	25-Feb-19	6800, 5600	6610, 5500, 5800																																		
<b>ECS Procurement</b>																																									
6610	ECS	ECS - Procurement	63	26-Feb-19	23-May-19	5650, 6600	5590, 6652, 6650																																		
<b>ECS Construction</b>																																									
6650	ECS	ECS - Construction & Testinq - Telecom Route 1 - Splicing (Intermittent)	105	17-Aug-22	18-Jan-23	6250, 5900, 6259, !	6850																																		
6652	ECS	ECS - Construction & Testinq - Telecom Routes 2 & 3	105	11-May-20	07-Oct-20	6030, 5950, 6610, !	6850																																		
<b>Distribution (&lt;=33kV)</b>																																									
<b>Distribution Segment x</b>																																									
<b>Dist Engineering/Planning</b>																																									
6420	Distribution	Distribution (Transmission Crossings) - Engineering	84	24-Dec-18	24-Apr-19	6200	6430, 5800																																		
<b>Dist Procurement</b>																																									
6430	Distribution	Distribution (Transmission Crossings) - Procurement	84	25-Apr-19	22-Aug-19	6420, 5650	5590, 6440																																		
<b>Dist Construction</b>																																									
6440	Distribution	Distribution (Transmission Crossings) - Construction & Testinq (Intermittent)	210	11-May-20	12-Mar-21	5900, 6430	7590																																		

<span style="background-color: yellow;">■</span> Completed Activity	<span style="color: red;">♥</span> Outstanding Milestone
<span style="background-color: #c8e6c9;">■</span> Outstanding Activity	<span style="color: red;">♥</span> Critical Path Milestone
<span style="background-color: #f44336;">■</span> Critical Path Activity	
<span style="border: 1px solid black; background-color: yellow;">◀</span> Completed Milestone	

DRAFT
